

LINVILLE RIVER RESTORATION PROJECT (LRRP) UPDATE November 20, 2019







In-channel work was completed September 18, 2019







Live Staking occurred November 12-15, 2019







>3,000 live stakes were purchased regionally and transported to the restoration project



FOREST SERVICE NC



Live stake species included:

- Silky Dogwood
- Silky Willow
- Elderberry
- Ninebark







Live stakes were prepped for installation by cutting the bottom to expose cambium







Live Stakes were planted on the restored river banks close to the water's edge












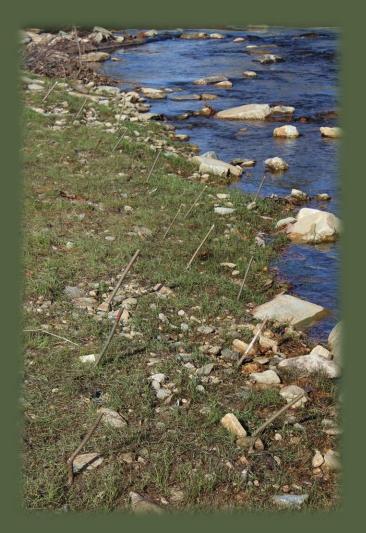







And both banks of the unnamed stream











Still needed:

- Planting bare root seedlings and salvage seedlings from Gill SF; planned for February-March 2020
- Construction fishing/hiking trail and information kiosks; planned for February-March 2020
- Biomonitoring macrobenthos/fish in Summer 2020 by NCDWR, WSS





LRRP Contact Information:

Web - <u>www.ncforestservice.gov/LinvilleRiverRestoration</u> Email - <u>ncfs.water@ncagr.gov</u>

NCFS Social Media

- FaceBook <u>https://www.facebook.com/NCForestService</u>
- Twitter <u>https://twitter.com/ncforestservice</u>

